



BUSINESS REQUIREMENTS DOCUMENT

Giga-Projects Municipal Services Platform

منصة الخدمات البلدية للمشاريع الكبرى

Business requirements for the unified municipal-services gateway serving Riyadh's giga projects, and its integration into the official Riyadh Region Municipality portal — alriyadh.gov.sa.

Version

1.0 (Draft for review)

Date

8 August 2026

Classification

Internal — Restricted

Reference

RRM-GPO-BRD-2026-001

§ Document Control

Item	Detail
Document title	Business Requirements Document — Giga-Projects Municipal Services Platform (منصة الخدمات البلدية للمشاريع الكبرى)
Reference	RRM-GPO-BRD-2026-001 · Version 1.0 (Draft) · 8 August 2026
Business owner	Giga Projects Office (GPO), Riyadh Region Municipality
Related assets	Working prototype (bilingual, fully interactive); portal design reference: alriyadh.gov.sa
Status	Draft for stakeholder review — pending approval by GPO, Digital Transformation Agency of the Amanah, and Portal Governance Committee

Revision history

Version	Date	Description
0.9	28 July 2026	Initial draft from prototype build (platform scope, roles, service catalog, SLA model, impact model)
1.0	8 August 2026	Added portal-integration requirements (alriyadh.gov.sa), unified visual identity, phasing and acceptance criteria

Approvals (pending)

Role	Name	Signature	Date
Director, Giga Projects Office	—		
Head of Digital Transformation	—		
Portal Governance (alriyadh.gov.sa)	—		

§ Contents

1	Executive summary	3
2	Background and strategic context	3
3	Business objectives and success measures	4
4	Scope	4
5	Stakeholders and user roles	5
6	Current state and problem statement	5

7	Proposed solution overview	6
8	Business requirements catalog	7
9	Integration with alriyadh.gov.sa	9
10	Non-functional requirements	11
11	Data, reporting and the impact model	11
12	Assumptions, constraints and dependencies	12
13	Risks and mitigations	12
14	Implementation roadmap	13
15	Acceptance criteria	13
16	Appendix — prototype screens and glossary	14

1 Executive Summary

Riyadh is delivering one of the largest coordinated urban-development programs in the world. Giga projects such as Diriyah, Qiddiya, New Murabba, King Salman International Airport and Expo 2030 Riyadh depend on hundreds of municipal decisions — survey decisions, plan approvals, building permits, infrastructure handovers, environmental clearances and operating licenses — whose timeliness directly gates construction schedules measured in billions of riyals.

The **Giga-Projects Municipal Services Platform** (منصة الخدمات البلدية للمشاريع الكبرى) is a single, bilingual gateway through which giga-project entities, developers, engineering offices, investors and operators submit, track and receive every municipal service relevant to a large project — against published service-level agreements (SLAs), with structured escalation, an auditable decision trail, and live measurement of economic impact.

A fully interactive prototype has been built and styled as a native section of the official municipality portal, **alriyadh.gov.sa**. This BRD records the business requirements embodied by that prototype and specifies the requirements for integrating the platform into the official portal: placement inside الخدمات الإلكترونية, unified sign-on (Nafath and portal accounts), the shared design system, unified notifications, the 940 contact channel, hosting, analytics, and compliance obligations.

38

Documented municipal services with published SLAs (2–28 working days)

5

Official end-to-end journeys — planning, building, investor, operation, industrial

–67%

Targeted reduction in average service time vs. pre-platform baselines

2 Background and Strategic Context

Vision 2030 and the Riyadh agenda. National strategy positions Riyadh among the world's ten largest city economies, with population targets approaching 15 million and a giga-project investment pipeline spanning culture, sport, aviation, housing and urban regeneration. Municipal enablement — permits, plans, inspections, licenses — is on the critical path of that pipeline.

The Giga Projects Office. The Amanah has established a dedicated Giga Projects Office (مكتب المشاريع الكبرى) as the single municipal counterpart for large projects: one registry of projects, one prioritized lane for their requests, one escalation route for cross-agency blockages (التحديات), and one accountable scoreboard of timeliness and impact.

The digital gap. Today these interactions are dispersed across general-purpose channels that were not designed for the scale, urgency or multi-entity coordination that giga projects require. There is no unified view of a project's municipal pipeline, no published giga-specific SLAs, and no measurement of the economic cost of delay.

Why integrate with alriyadh.gov.sa. The official portal is the Amanah's front door: it carries the trusted brand, the unified design system, national sign-on, the 940 channel, the myCity app ecosystem and portal governance. Launching the platform as a portal section — rather than a stand-alone site — inherits that trust and infrastructure from day one, and keeps a single citizen- and business-facing digital estate.

3 Business Objectives and Success Measures

#	Objective	Success measure (target)
O1	Cut municipal service time for giga projects	Average processing $\leq$ 8 working days (baseline $\approx$ 25); catalog-level reduction $\geq$ 60%
O2	Deliver decisions within published SLAs	SLA compliance $\geq$ 90%; first response $\leq$ 2 working days
O3	Resolve cross-agency blockages fast	Challenge closure rate $\geq$ 85% within SLA (15 working days)
O4	Full digital, paperless intake and decisioning	100% of requests digital end-to-end; zero paper documents
O5	Customer trust and satisfaction	Satisfaction $\geq$ 4.2 / 5 measured per closed request
O6	Make impact visible and accountable	Delay-cost model published with methodology; impact dashboard live for GPO and leadership
O7	One front door via the official portal	Platform discoverable and accessible from alriyadh.gov.sa with unified sign-on

4 Scope

4.1 In scope

- **Public section** (inside the portal): platform landing with the services catalog (دليل الخدمات) and the interactive developer/investor journeys (رحلات المطور والمستثمر العقاري).
- **Customer portal**: guided request wizard, my-requests tracking, journey canvas with live progress, resubmission, challenges, notifications, satisfaction rating, profile and delegation.
- **Staff workspace**: triage queue, three-pane review workspace, document verification, external referrals, decisions with conditions/co-sign, SLA clocks and escalation.
- **Management**: GPO dashboard, projects registry, KPIs, reports, service-catalog administration, audit log, settings (holidays, SLA policy), impact dashboard (أثر المنصة).
- **Executive view**: boardroom summary with impact headline figures and weekly highlights.
- **Portal integration**: identity, design system, hosting, notifications, 940/chat, myCity, open data, analytics (Section 9).

4.2 Out of scope (this phase)

- Fee payment execution (SADAD integration) — fees are displayed; collection remains on existing rails until Phase 2.
- Automated GIS parcel validation and field-inspection scheduling (Phase 2 with Amanah GIS).
- Direct system-to-system integrations with external entities (water, power, environment authorities) beyond the referral workflow — Phase 2 via the Government Service Bus.
- Non-giga (general public) municipal services — these remain in the portal's existing e-services.

Prototype status. The current build demonstrates the full experience with fictional data on a client-side data store by design. Its data layer is a swappable repository interface so that Phase 1 replaces storage with Amanah CRM/REST services without UI change.

5 Stakeholders and User Roles

Role	Description	Key capabilities
Project representative (ممثل مشروع)	Authorized user of a registered project. Personas: giga-entity representative, real-estate developer, engineering office (delegate), investor, operator.	Submit/track requests, journeys, challenges, ratings, delegation scope
Amanah specialist (أخصائي دراسة)	Reviews assigned requests within SLA; verifies documents; refers externally; prepares decisions.	Queue, review workspace, returns, referrals, decision drafts
Platform manager / GPO (مدير المنصة)	Section head at the Giga Projects Office; owns catalog, SLAs, escalations and reporting; co-signs sensitive decisions.	Dashboards, registry, KPIs, impact, catalog & settings, audit
External entity reviewer (جهة خارجية)	Receives scoped referrals (e.g., utilities, environment) and returns opinions within referral SLA.	Referral inbox, respond with opinion/conditions
Executive viewer (مطالع تنفيذي)	Leadership; consumes summaries only.	Executive summary, impact headline, print brief

Other stakeholders: Portal Governance Committee (alriyadh.gov.sa), Digital Transformation Agency of the Amanah, giga-project owner companies, external government entities, Digital Government Authority (standards), National Cybersecurity Authority (controls).

6 Current State and Problem Statement

Pain point	Business consequence
No single lane for giga-project requests; they queue with general workload	Critical-path permits wait behind routine transactions; schedule slip on multi-billion-riyal programs
SLAs not published per service; no live clocks or escalation bands	No accountability for timeliness; disputes about elapsed time; surprises instead of early warning
Cross-agency blockages have no owner or workflow	Utility relocations and clearances stall for months; no record of cause or resolution
Document requirements discovered iteratively	High return/resubmission rates; wasted review cycles
No project-level view of the municipal pipeline	Neither the entity nor the GPO can see everything blocking a project at once
Delay cost invisible	Investment case for process improvement cannot be made; wins go unmeasured

7 Proposed Solution Overview

One platform, five experiences, one data spine:

Module	What it does
Services catalog (دليل الخدمات)	38 documented services across the project lifecycle — pre-development (planning, survey decisions, master plans), during delivery (building/demolition permits, infrastructure design and handover, environmental construction permits, enablement permits such as cranes, hoarding, road closures, dewatering, utility relocation), and post-completion (operating licenses, activity licensing, periodic compliance, renewals). Each service publishes purpose, prerequisites, required documents with accepted formats, fees model, supporting entities and SLA in working days.
Journeys (رحلات المطور والمستثمر)	Five official journeys rendered as an interactive canvas of connected stages (serpentine on desktop, spine on mobile): planning (7 steps and three plan-approval paths), building (5), investor (6), operation & asset management (7), industrial (5). Signed-in customers see their project's live position («أنت هنا»), completed and blocked stages, and can start any service from its stage.
Request wizard	Guided, validating intake: project and phase selection, dynamic service forms, document upload with format checks, review and declaration, drafts, and a tracking number on submission.
Lifecycle engine	Twelve request states from draft to closure with role-guarded transitions; SLA clocks on a Sunday–Thursday calendar with official holidays; the clock pauses while a request is returned to the customer; escalation bands (green/amber/red) with automatic GPO escalation at breach; fast-track lane halving SLAs for giga entities; co-sign rule for fee-bearing or fast-track decisions; permit numbering on approval.
Review workspace	Three-pane specialist screen: request summary and SLA clock; document verification checklist; decision pane with approve/return/reject/refer, conditions, regulation references and templates.
Challenges (التحديات)	Structured intake of cross-agency blockages tied to a project and optionally a request; categories, owner assignment, SLA, escalation to GPO coordination, resolution record.
Impact (أثر المنصة)	Delay-cost model computed live from decided requests: working days saved vs. pre-platform baselines, estimated savings (SAR), investment value accelerated, estimated GDP contribution, jobs supported — with a per-request impact ledger, methodology disclosure, and honest estimated/measured labeling (Section 11).
Reporting & audit	KPI engine (processing time, SLA compliance, first response, on-time rate, challenge closure, satisfaction), weekly trends, printable executive brief, and a full audit log of administrative and decision actions.
Experience layer	Arabic-first RTL with full English mirror; the portal's design system (Section 9); accessibility and mobile hardening; command palette; theme/accent/density personalization.

8 Business Requirements Catalog

Priorities follow MoSCoW: **M** must have · **S** should have · **C** could have. All requirements below are demonstrated in the prototype unless marked otherwise.

8.1 Public section and catalog

ID	Requirement	Pri
BR-001	The public landing shall present the services catalog with phase filter tabs (all / pre-development / during delivery / post-completion), free-text search, and a service detail view showing prerequisites, required documents and formats, fees note, supporting entities and SLA.	M
BR-002	The public landing shall present the five official journeys as a connected, read-only visualization; selecting a journey routes to sign-in and then the full interactive canvas.	M
BR-003	Every public page shall be available in Arabic (default, RTL) and English with equivalent content.	M

8.2 Customer portal

ID	Requirement	Pri
BR-010	A signed-in project representative shall submit any catalog service through a guided wizard with per-service dynamic forms, document upload validated against declared formats, a review step and a legal declaration; incomplete submissions shall be blocked with actionable errors.	M
BR-011	Drafts shall be savable and resumable; a submitted request shall receive a unique tracking number and appear in "My requests" with state, SLA countdown and macro-progress rail.	M
BR-012	The journey canvas shall map the customer's actual requests onto journey stages (completed / in progress / action required / upcoming), flag the current stage, and offer stage-level actions (start request, continue draft, view request/decision).	M
BR-013	When a request is returned, the customer shall see the reasons and missing items, amend and resubmit; the SLA clock shall be visibly paused during customer action.	M
BR-014	Customers shall log challenges (تحديات) tied to a project/request with category and description, and track their resolution.	M
BR-015	On closure, the customer shall be invited to rate satisfaction (1–5) with optional comment; ratings feed KPI-5.	S
BR-016	Engineering offices shall act under an explicit, visible delegation scope limited to authorized services.	S

8.3 Staff and decisions

ID	Requirement	Pri
BR-020	Specialists shall work from a prioritized queue (inbox / mine / decisions due / returned) ordered by SLA urgency, with fast-track requests visually distinguished.	M

ID	Requirement	Pri
BR-021	The review workspace shall present summary, documents and decision panes together; every document shall be individually verifiable (accept / flag) before decision.	M
BR-022	Available decisions shall be state- and role-guarded: return with reasons, refer externally with scope and due date, approve with optional conditions, reject with regulation reference. Fee-bearing or fast-track approvals by a specialist shall require GPO co-sign.	M
BR-023	External referrals shall create a scoped work item for the external entity with its own SLA; the parent request shall show referral status and returned opinions.	M
BR-024	Approvals shall issue a numbered permit/decision document; all decisions shall be recorded in the audit log with actor, timestamp and payload.	M
BR-025	SLA breaches shall auto-escalate to the GPO dashboard; every breach shall carry cause visibility (elapsed vs. paused days).	M

8.4 Management, catalog and settings

ID	Requirement	Pri
BR-030	The GPO shall maintain the projects registry (register, enable, hold, archive) with sector, phase, location and giga designation.	M
BR-031	The GPO shall administer the service catalog: SLA days and fast-track eligibility editable with an audit trail; changes apply to new requests only.	M
BR-032	Dashboards shall show live KPIs with period comparison, weekly submission/decision trends, breakdowns by service and sector, and drill-through to underlying requests.	M
BR-033	Settings shall govern the working calendar (weekend, official holidays) used by every SLA computation.	M
BR-034	A printable executive brief shall summarize KPIs, impact headline and escalations for leadership.	S

9 Integration with alriyadh.gov.sa

The platform launches as a native section of the official portal. The prototype already implements the portal's visual identity end-to-end (measured from the live site: palette, header anatomy, typography scale, component geometry). The requirements below complete the operational integration.

9.1 Placement and navigation

ID	Requirement	Pri
IR-001	The platform shall be reachable from the portal's الخدمات الإلكترونية menu and services hub as "خدمات المشاريع الكبرى", with a featured entry on the e-services landing.	M
IR-002	Canonical hosting shall be under the portal domain — path alriyadh.gov.sa/giga-services (or subdomain giga.alriyadh.gov.sa) behind the portal's edge (TLS, WAF, CDN); no third-party domain shall be user-visible.	M
IR-003	Each catalog service shall be listed in the portal's service directory with a deep link that opens the platform wizard pre-selected on that service (e.g. .../giga-services#/wizard?service=building-permit).	M
IR-004	The platform shall render the portal's global chrome: top utility bar, header/mega-menu, breadcrumbs (الرئيسية ← الخدمات الإلكترونية ← خدمات المشاريع الكبرى), and the portal footer — sourced from the portal design system package, not duplicated.	M

9.2 Identity and access

ID	Requirement	Pri
IR-010	Customer sign-in shall use the National Single Sign-On (Nafath — النفاذ الوطني الموحد) and existing portal accounts; a company representative shall bind to a registered project via GPO-approved authorization.	M
IR-011	Staff access shall federate with the Amanah identity provider used for بريد الموظفين (SSO, MFA); platform roles map to IAM groups (specialist, GPO manager, external reviewer, executive).	M
IR-012	External entity reviewers shall access through the government interconnection channel or scoped federated accounts, limited to their referrals.	M
IR-013	Session, consent and privacy notices shall follow portal policy (سياسة الخصوصية) and PDPL requirements.	M

9.3 Channels and services around the platform

ID	Requirement	Pri
IR-020	Notifications (submission, state change, return, decision, escalation) shall be delivered through the portal's unified notification gateway — SMS, email and portal inbox — in the customer's language.	M
IR-021	The 940 contact center and the portal's chat تحديث معنا shall be able to look up a request by tracking number and log a challenge on the customer's behalf.	M

ID	Requirement	Pri
IR-022	The myCity app (تطبيق مدينتي) shall deep-link into request tracking; push notifications mirror the unified gateway.	S
IR-023	Anonymized, aggregated platform indicators (volumes, SLA compliance, impact headline) shall be published to the portal's open-data section (البيانات المفتوحة) on a monthly cycle.	S
IR-024	Usage analytics shall flow into the portal's unified analytics; the platform contributes to إحصائيات البوابة.	S
IR-025	Public copy (service descriptions, journey texts) shall be governed through the portal content workflow, bilingual, with GPO as content owner.	M

9.4 Platform-to-core integrations (Phase 1–2)

ID	Requirement	Pri
IR-030	The prototype's repository layer shall be replaced by Amanah CRM/case-management REST services behind the same interface (requests, projects, documents, decisions, notifications) — the UI contract is already adapter-based.	M
IR-031	Document storage shall move to the Amanah ECM with virus scanning, retention policy and evidential integrity.	M
IR-032	External-entity referrals shall ride the Government Service Bus where counterpart integrations exist; the manual referral workflow remains the fallback.	S
IR-033	Fee-bearing services shall integrate SADAD billing at decision time (Phase 2); until then fee notes display and collection stays on current rails.	S
IR-034	The projects map shall consume Amanah GIS layers for project boundaries (Phase 2), replacing the stylized map.	C

10 Non-Functional Requirements

ID	Category	Requirement
NFR-01	Language	Arabic-first RTL with full English mirror; every label, notification and document bilingual; Hijri/Gregorian dates as per portal convention.
NFR-02	Accessibility	WCAG 2.1 AA: keyboard-complete flows, visible focus, reduced-motion support, contrast-checked palette, screen-reader landmarks (prototype implements these patterns).
NFR-03	Performance	First meaningful render ≤ 3 s on standard broadband; interactions ≤ 200 ms; production build code-split (the single-file bundle is a prototype packaging choice).
NFR-04	Responsiveness	Full function from 390 px phones to desktop; touch targets ≥ 40 px; no horizontal panning.
NFR-05	Availability	99.9% monthly for customer-facing functions; maintenance windows per portal policy.
NFR-06	Security	NCA Essential Cybersecurity Controls; OWASP ASVS L2; full audit trail; least-privilege roles; data hosted in-Kingdom (PDPL).
NFR-07	Auditability	Every state change and administrative action attributable (who/when/what) and retained per records policy.
NFR-08	Browsers	Evergreen Chrome/Edge/Safari/Firefox, latest two versions; iOS and Android WebView via myCity.

11 Data, Reporting and the Impact Model

The platform measures itself. Six operational KPIs are computed live (average processing time, SLA compliance, first-response time, on-time rate incl. open requests, challenge closure, satisfaction), and an **economic impact model** converts time saved into money terms using a delay-cost methodology:

- Every service carries a documented pre-platform baseline duration; every project carries an indicative investment value and a daily delay-cost factor; every service carries a critical-path weight.
- For each approved request: *days saved* = *baseline* – *actual net working days*; *savings* = *days saved* × *project value* × *daily factor* × *critical-path weight*; accelerated value and GDP/jobs contributions derive from standard economic coefficients.
- Every figure is labeled **estimated** (modeled) or **measured** (directly observed); the methodology is published in full inside the product, and a per-request impact ledger makes headline numbers auditable.

In production, baselines, project values and coefficients shall be replaced with officially approved figures, and the model reviewed by the Amanah's economics function before external publication (see R-05).

12 Assumptions, Constraints and Dependencies

ID	Statement
A-01	The GPO operating model (single counterpart, prioritized lane, published SLAs) is approved policy before go-live.
A-02	Giga entities will nominate authorized representatives and accept digital-only submission.
A-03	Portal governance grants the platform a section under الخدمات الإلكترونية and access to the design-system package.
C-01	All production data resides in-Kingdom; no external CDNs or trackers beyond portal-approved tooling.
C-02	SLA definitions are bounded by regulation; the platform publishes and measures them but does not override regulatory time limits.
D-01	Nafath/SSO onboarding, Amanah IdP federation, unified notification gateway, CRM/ECM environments, GSB connectivity — owned by the Digital Transformation Agency.
D-02	940 and chat scripts updated to recognize the platform's tracking numbers.

13 Risks and Mitigations

ID	Risk	Impact	Mitigation
R-01	SLA commitments published before operational readiness	High	Soft-launch with two pilot entities; publish SLAs per service wave after two green weeks
R-02	External entities do not act within referral SLAs	High	Escalation to GPO coordination committee is built-in; referral performance is reported by entity
R-03	Integration timeline (SSO/CRM/ECM) slips	Medium	Adapter architecture allows portal-hosted pilot with interim identity while integrations land
R-04	Duplicate channels confuse customers during transition	Medium	Single-front-door policy: portal directory deep-links only to the platform for giga services; legacy channels redirect
R-05	Impact figures quoted externally without context	Medium	Estimated/measured labeling, published methodology, economics-function sign-off before any external use
R-06	Content drift between portal directory and platform catalog	Low	Catalog is the single source; directory entries generated from it (IR-003, IR-025)


14 Implementation Roadmap

Complete Phase 0 — Prototype Full interactive demonstration: 38 services, 5 journeys, lifecycle engine, workspaces, dashboards, impact model, portal visual identity, bilingual, mobile-hardened.	~ 3 months Phase 1 — Portal launch (MVP) Hosting under alriyadh.gov.sa; Nafath + staff SSO; CRM/ECM adapters replace demo store; unified notifications; 940/chat lookup; content governance; pilot with two giga entities and a 12-service wave.	~ 6 months Phase 2 — Core integrations Full 38-service catalog live; SADAD fees; GSB referrals to first external entities; GIS layers; myCity deep links; open-data feed; onboarding of all registered giga projects.	Ongoing Phase 3 — Scale & optimize Additional entities and services; SLA tightening from measured performance; predictive workload; assisted drafting for specialists; annual impact report.
--	---	--	---


15 Acceptance Criteria (Phase 1 gate)

ID	Criterion
AC-01	A pilot-entity representative signs in via Nafath from alriyadh.gov.sa, submits a building-permit request end-to-end digitally, and receives the tracking number by SMS/email/portal inbox.
AC-02	A specialist processes the request in the workspace within SLA; the customer sees each state change with a live SLA clock; a return pauses the clock until resubmission.
AC-03	A fee-bearing or fast-track approval requires and records GPO co-sign, and issues a numbered decision document stored in ECM.
AC-04	An SLA breach escalates automatically and appears on the GPO dashboard with cause visibility; a challenge logged via 940 appears in the challenges module.
AC-05	The section renders inside the portal chrome, passes WCAG 2.1 AA checks on key flows, and functions fully in Arabic and English from a 390 px phone to desktop.
AC-06	KPI and impact dashboards compute from live pilot data; every headline figure traces to its per-request ledger entries.

16 Appendix A — Prototype Screens

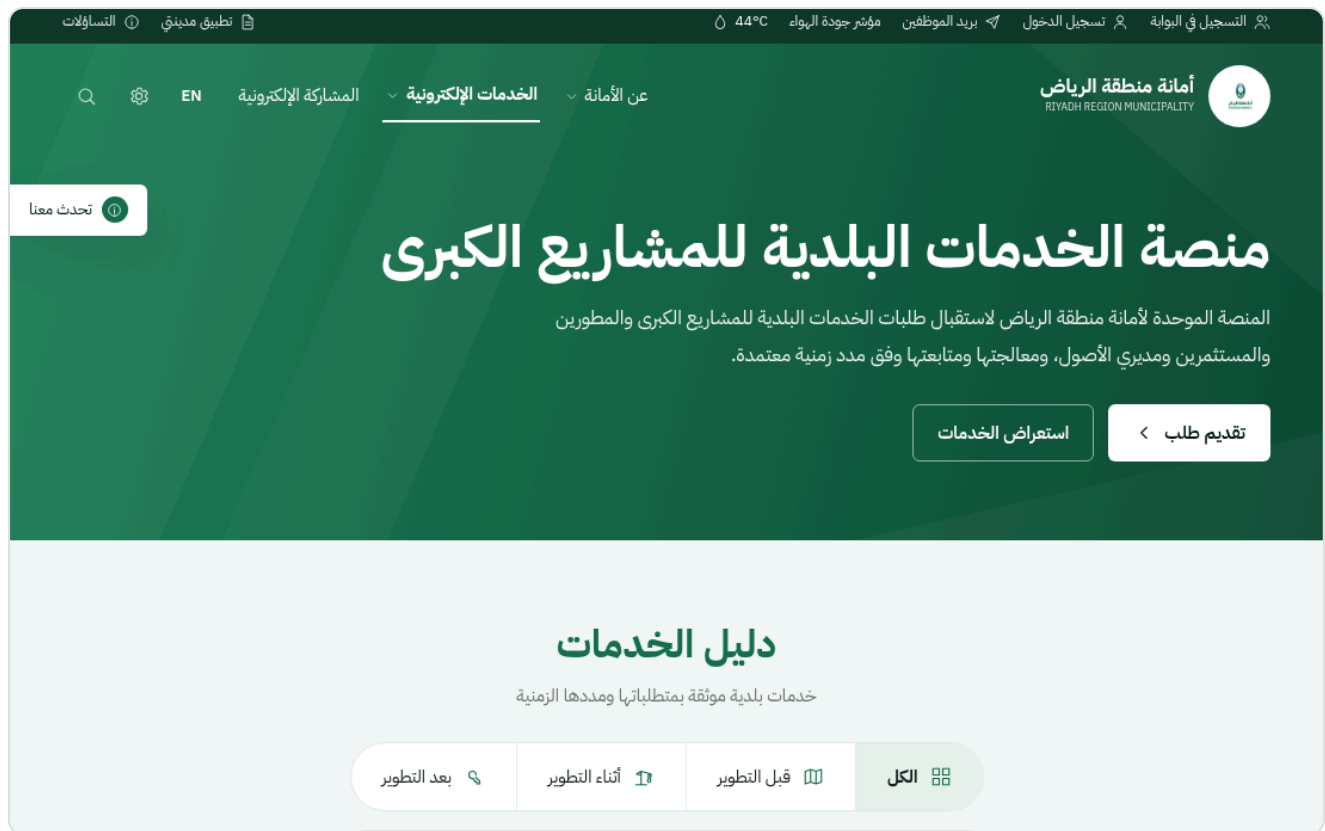


A.1 — Public section rendered in the alriyadh.gov.sa design language: utility bar, portal header with «الخدمات الإلكترونية» active, services catalog with phase tabs.

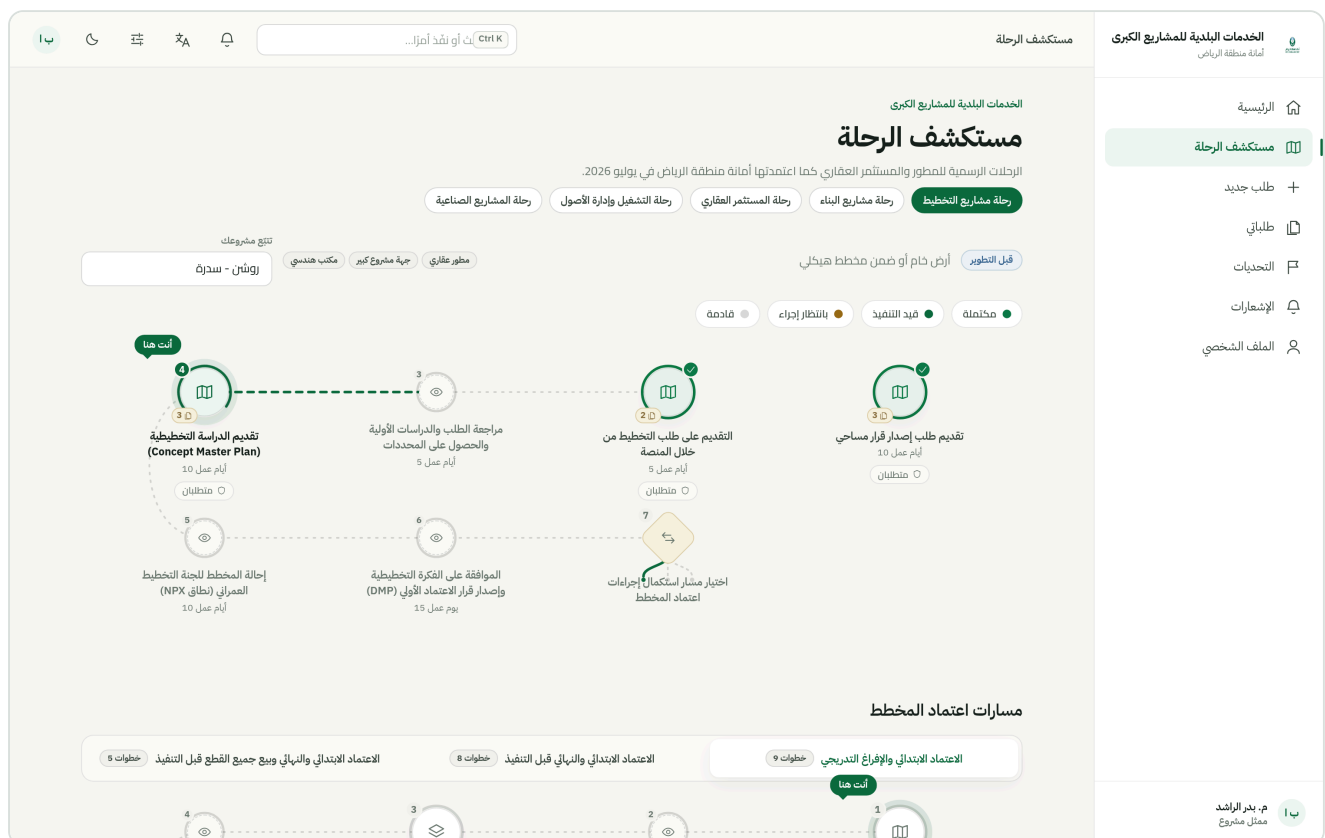

A.2 — Journey canvas: the planning journey with live per-stage status mapped from the customer's project, current position («أنت هنا»), and the three plan-approval paths.

16 Appendix A – Prototype Screens (continued)

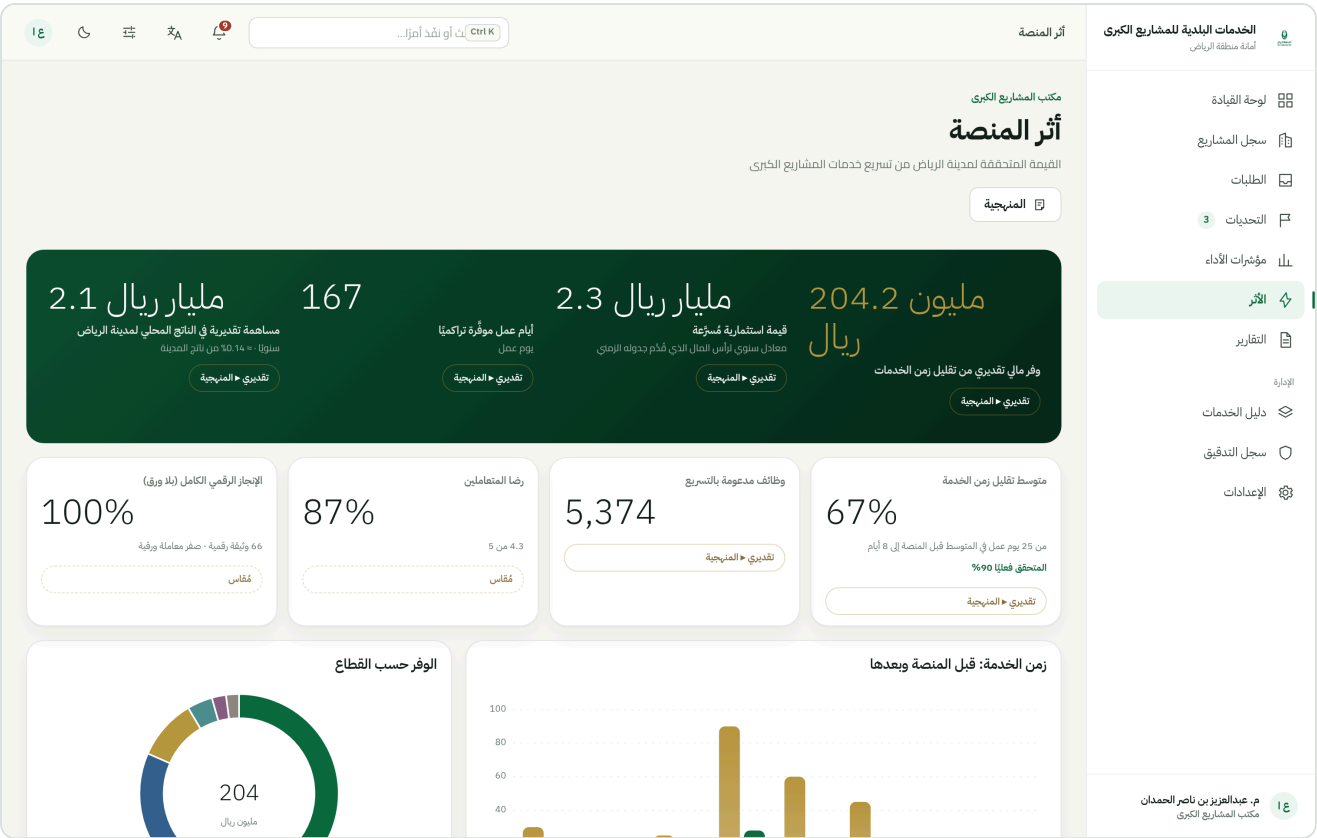

A.3 — Impact dashboard «أثر المنصة»: delay-cost headline figures, estimated/measured labeling, sector breakdown and the per-request impact ledger.

Appendix B – Glossary

Term	Definition
Amanah (الأمانة)	أمانة منطقة الرياض — Riyadh Region Municipality
GPO (مكتب المشاريع الكبرى)	Giga Projects Office; single municipal counterpart for giga projects.
SLA	Service-level agreement — published duration in working days (Sun–Thu, excluding official holidays).
Fast track (مسار الأولوية)	Priority lane for giga-entity requests on eligible services; SLA halved; decisions co-signed.
Challenge (تحدي)	A structured cross-agency blockage record owned to resolution by the GPO.
Nafath (النفذ الوطني الموحد)	National single sign-on service.
GSB	Government Service Bus — the national interconnection channel for entity-to-entity integration.
PDPL	Personal Data Protection Law of Saudi Arabia.
Delay-cost model	Valuation of each saved working day as a fraction of affected project value, weighted by the service's critical-path share.

Prototype disclaimer. The accompanying demonstration uses fictional projects, requests, users and figures. It is not the official website of Riyadh Region Municipality, and no figure in it constitutes an official statistic.
